



| REF. NUMBER | | BILL OF MATERIAL | | | | | | | | | |
|---------------------------|-----|------------------|---------------|-----------|--------------------|----------------|------------|------------|--------------|--------|--|
| QTY | NO. | SHIPPING BILL | | SHOP BILL | | | | | | | |
| | | NO. | ERECTION MARK | NO. | SHAPE | MATERIAL GRADE | LENGTH | ASSY. MARK | REMARKS | WEIGHT | |
| 20 | 1 | 20B250 | | | BEAM | | | | SQ-2 | | |
| | | | | 1 | W14X22 | A992 | 17'-4 1/4" | 20B250 | Red 220R-345 | 383 | |
| | | | | 5 | L3X3X1/4 | A36 | 1-1 3/4" | a471 | | 28 | |
| | | | | 5 | L3X3X1/4 | A36 | 1-0 1/8" | a656 | | 25 | |
| | | | | 2 | PL3/8"X3 1/2" | A36 | 0-9" | p36 | | 7 | |
| | | | | 5 | PL1/4"X4" | A36 | 0-4" | p330 | | 6 | |
| | | | | 1 | PL1/4"X2 3/16" | A36 | 0-5" | p472 | | 1 | |
| | | | | 1 | BPL1/4"X11 1/8" | A36 | 7-0 1/4" | pb85 | | 66 | |
| | | | | 1 | BPL1/4"X11 1/8" | A36 | 10-0" | pb86 | | 94 | |
| | | | | 1 | BPL1/4"X16 1/4" | A36 | 3-2 1/2" | pb105 | | 43 | |
| | | | | 1 | BPL1/4"X16 1/4" | A36 | 10-0" | pb106 | | 136 | |
| | | | | 6 | 3/4" A325N_TC BOLT | | 0-1 3/4" | | Site | | |
| TOTAL WEIGHT THIS DRAWING | | | | | | | | | | 788 | |

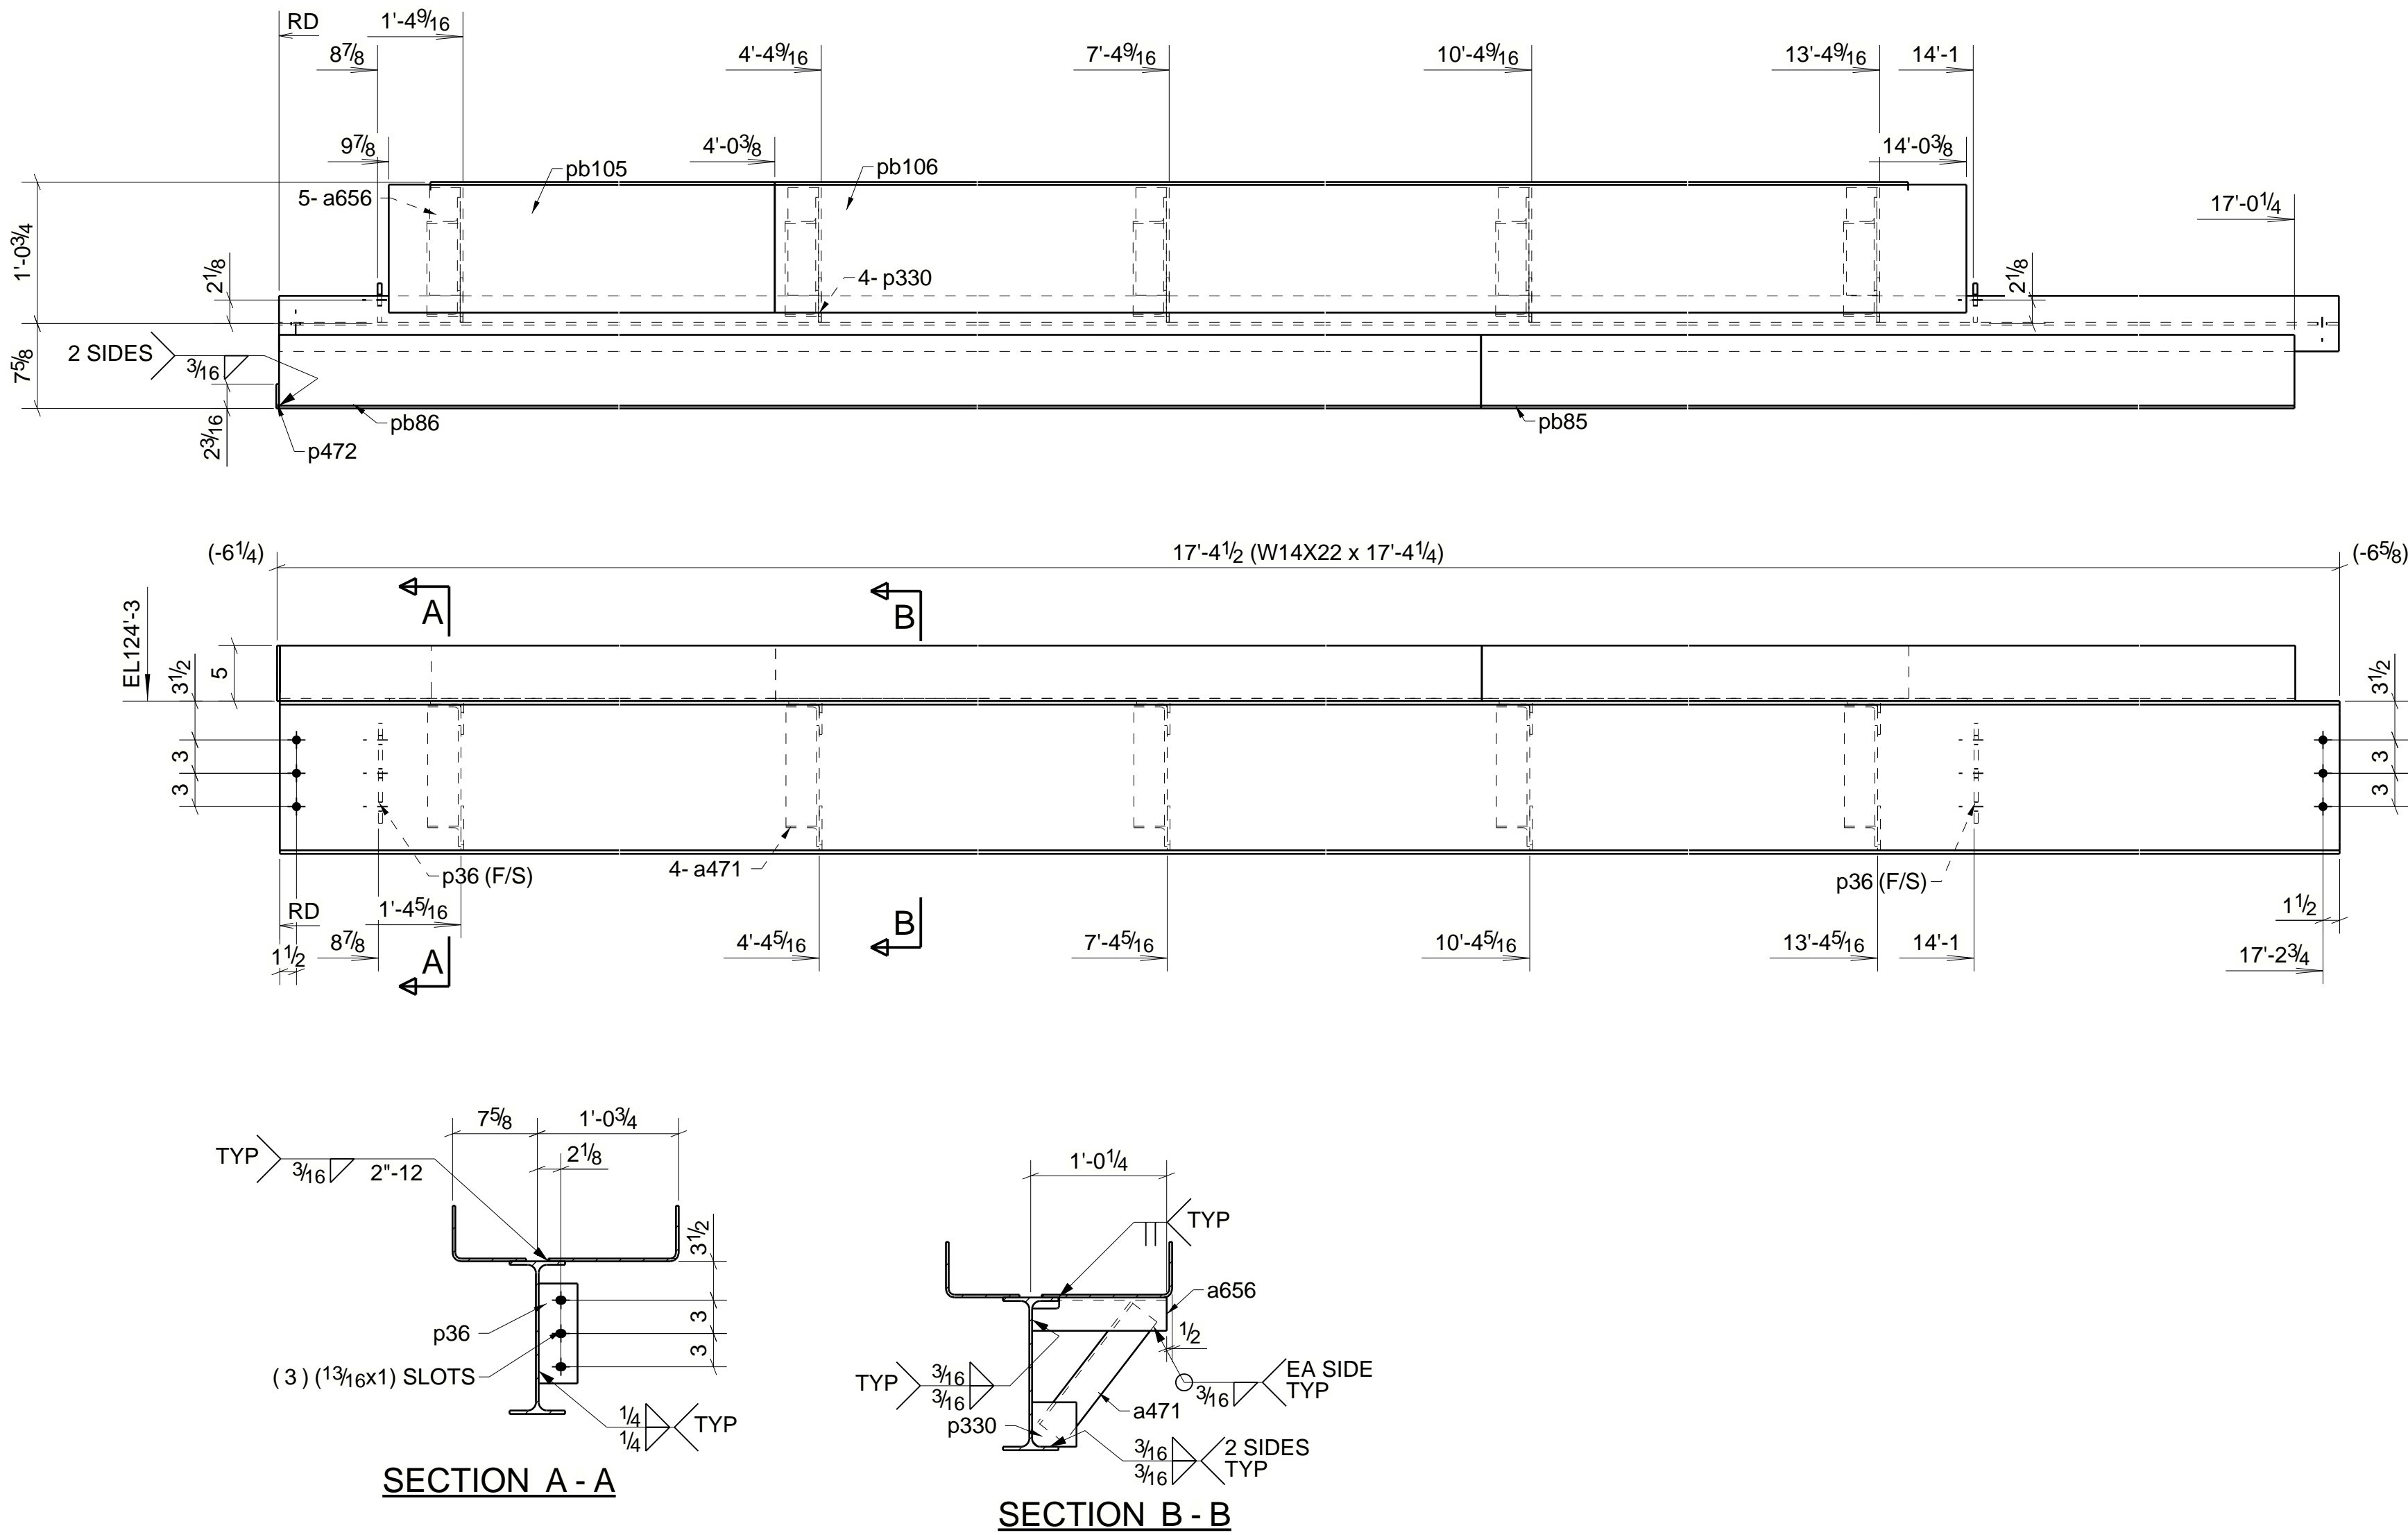

ONE - BEAM - 20B250

| | | | |
|------------------------------|---|-----------------|---------------------|
| E-SHEET REFERENCE | | | |
| MATERIAL (UNLESS NOTED) | A | 10/03/2022 | ISSUED FOR APPROVAL |
| A36 | REV. | DATE | DESCRIPTION |
| SURFACE PREPARATION | REVISION AND ISSUE RECORD | | |
| SSPC-SP2 |  | | |
| SHOP PAINT | Red 220R-345 | | |
| SHOP CONNECTIONS/ ELECTRODES | PROJECT WACO HIGH SCHOOL | | |
| WELDS/E70XX | CUSTOMER Rogers O'Brien Const Co Inc | | |
| | LOCATION 2020 N 42nd St, Waco, TX 76710 | | |
| | ARCH/ENG O'CONNELL ROBERTSON | | |
| | DETAILS BEAM | | |
| FIELD CONNECTIONS (U.N.O.) | DETAILER MJC | DATE 10/03/2022 | JOB NO. |
| 3/4 A325N_TC | CHECKER AJM | DATE 10/03/2022 | DRWG. NO. |
| | PM Dwayne Reed | | 32-22017 |
| | | | 20B250 |
